

CLINIC CONSTRUCTION UPDATE

10/16/2015



- Paving in the north lot should be done by end of week. 2 paths connecting the existing and new parking lots are planned.
- Sidewalks are 95% complete
- Landscaping is starting Monday, black dirt being end of this week.
- On the interior 2nd floor has significant flooring down and is being cleaned.
- Flooring is well progressed on 3 as well and will begin on 1st floor in 2 weeks.
- Furniture install is starting today and the audio booths have arrived.

As always, if you have questions or concerns about the project, email info@lrhc.org or call 218.736.8191.

712 Cascade St S
Fergus Falls, MN 56537
(218) 736-8000
www.lrhc.org




Lake Region
HEALTHCARE

Vision. Integrity. Award winning care.

Progress Report Through 10/13/15

- 3rd Floor- Interior Finishes ongoing. Electrical Devices being installed.
- 2nd Floor – Flooring is complete through all areas but 2-4. Plumbing and Electrical devices being installed. McGough beginning cleanup and pre punch items.
- 1st Floor – Painting/ wall covering ongoing, Millwork is being installed along with Ceiling grid. Lights and Diffusers are following grid.
- RTU's are being prepped for start-up.
- Elevators are nearing completion and inspection for construction use.
- Ornamental stair and glass railing ongoing in lobby.
- North Parking lot curb and Base complete ready for Asphalt this week.

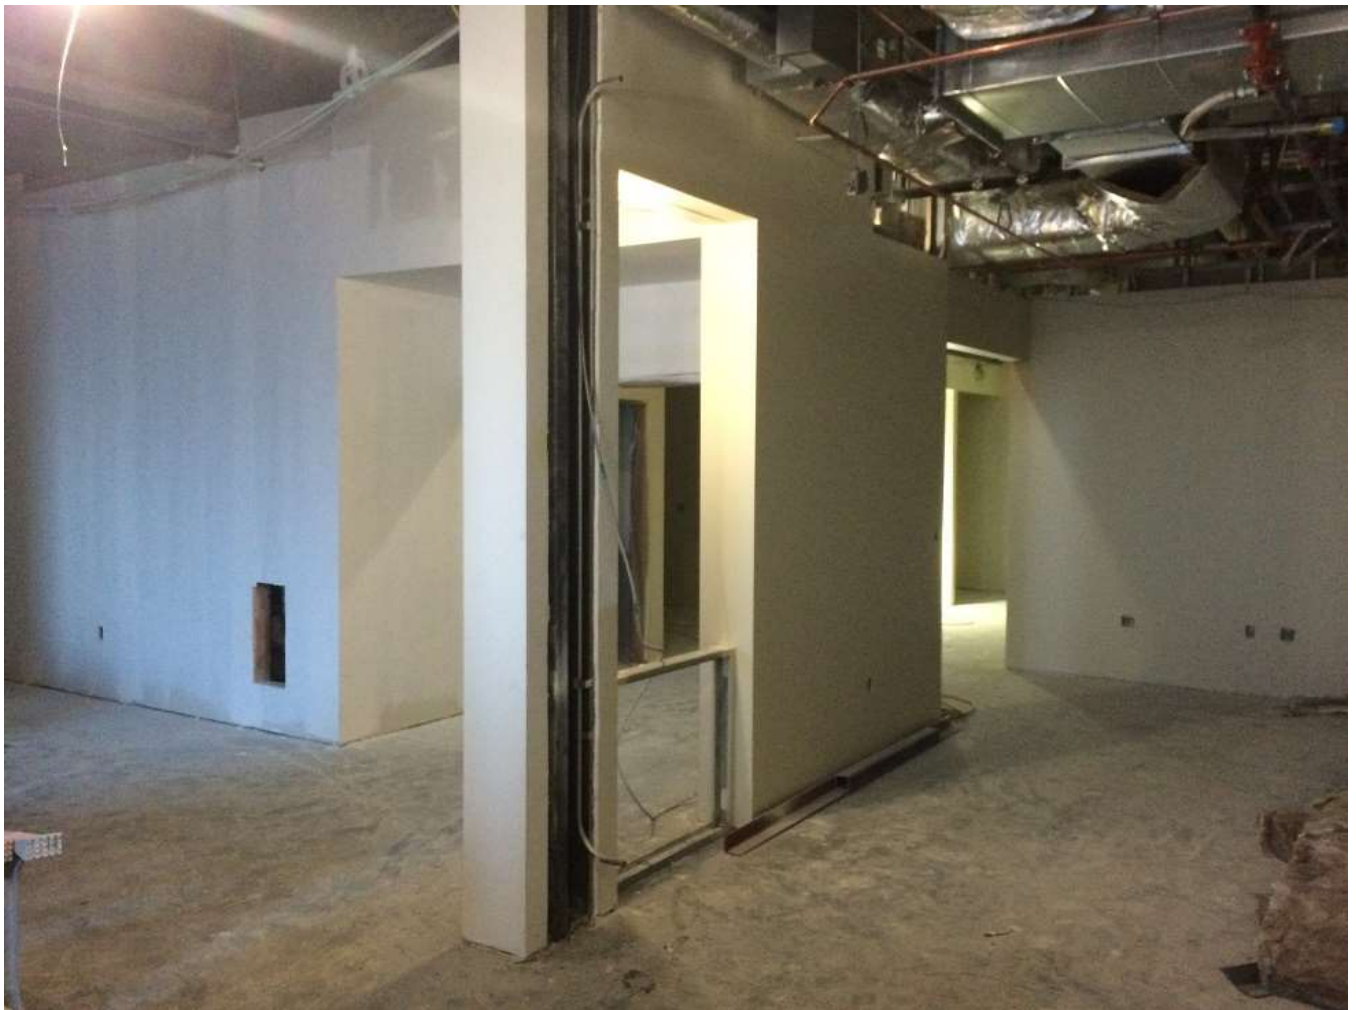

First Level Seq. 3-3 painting progress.

Progress Report Through 10/13/15



Sidewalks and Curb in North Parking lot.

Progress Report Through 10/13/15



Room Finishes on Second Floor Surgical Area.

Progress Report Through 10/13/15



Corridor Finishes on second floor.

Progress Report Through 10/13/15



Corridor Finishes on Second level Surgical area.

Progress Report Through 10/13/15



In Floor Scale Installed with flooring.

Progress Report Through 10/13/15



Electrical Devices and Plumbing Devices being installed.

Progress Report Through 10/13/15



Corridor Finishes in place.
