

Construction Progress Update Through 3/25/15

- Steel erection ongoing in seq 3
- Underground plumbing completing seq 1 starting seq 2
- Plumbers core drilling on second floor of seq 1
- Fireproofing being applied in seq 1
- Seq 2 2nd and 3rd floor decks poured
- Electricians laying underground and in deck conduits
- Framers laying track and framing walls in seq 1



Steel erection seq 3

Construction Progress Update Through 3/25/15




Deck poured 2nd level seq 2

Construction Progress Update Through 3/25/15



Fireproofing applied 2nd level seq 1

Construction Progress Update Through 3/25/15

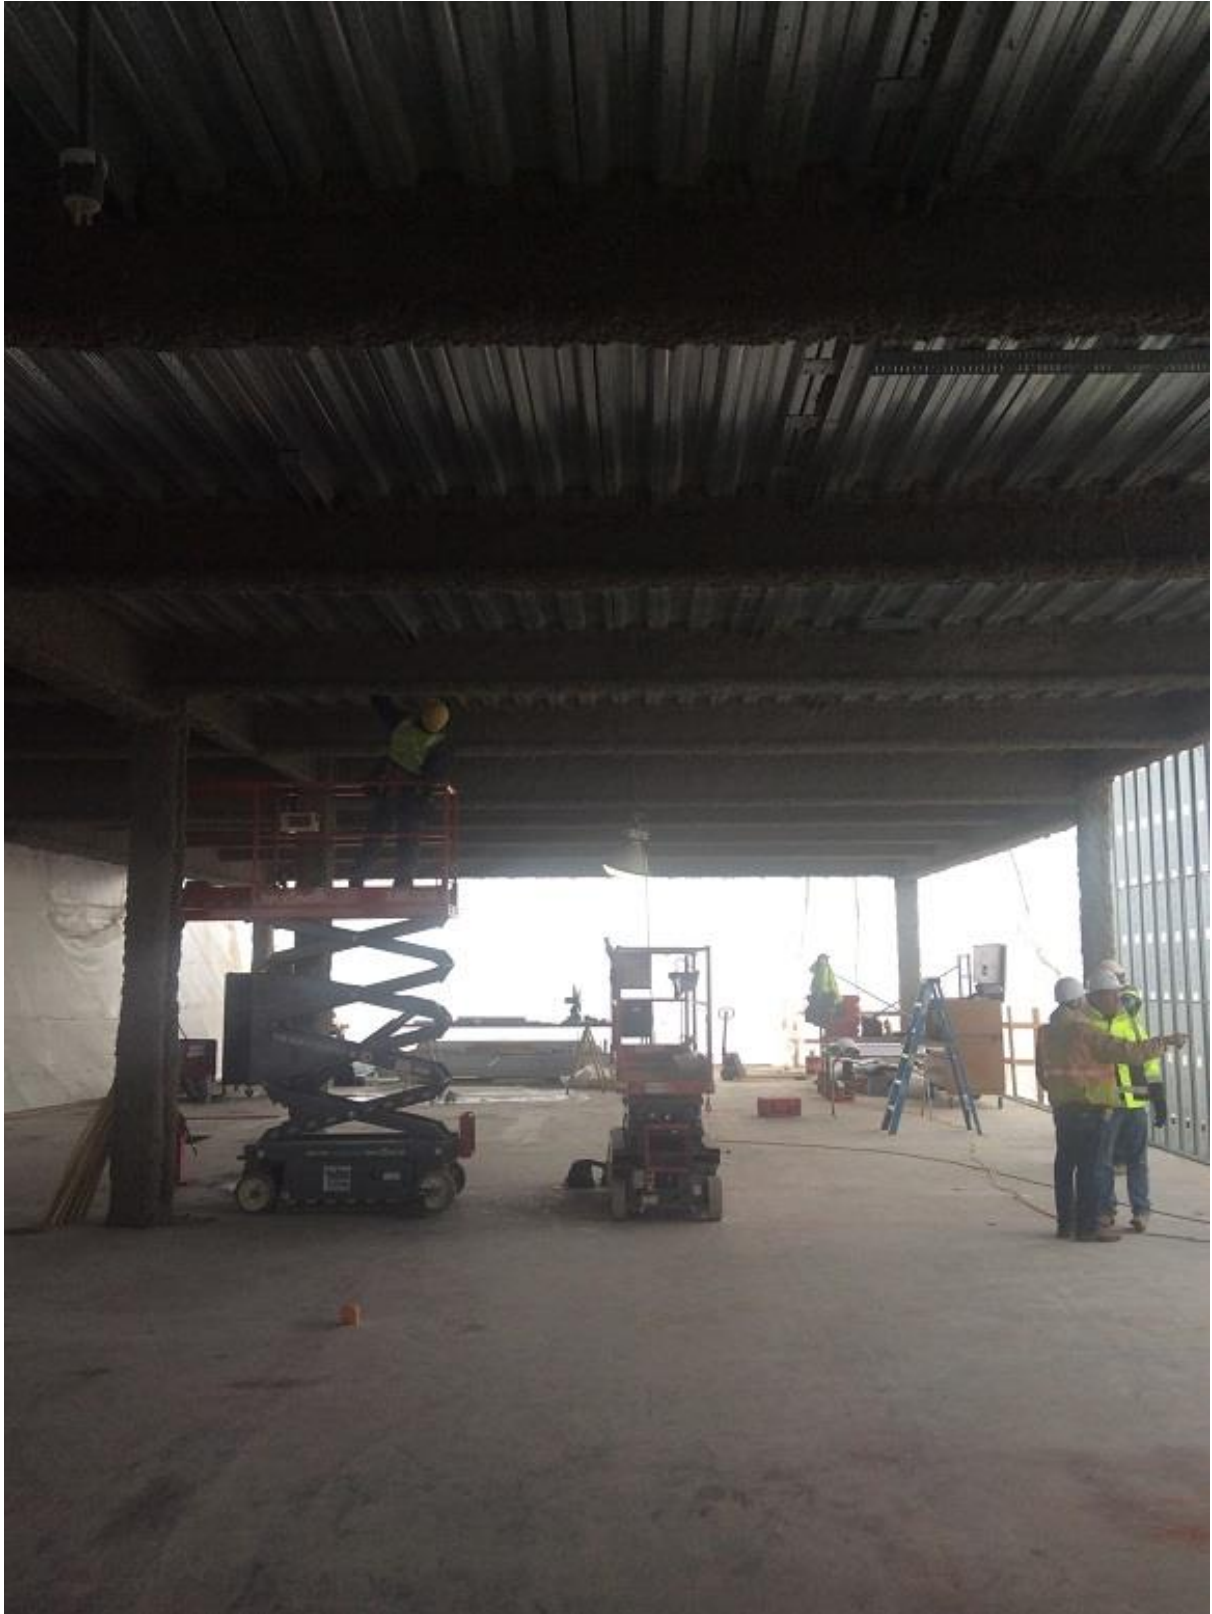

Exterior wall framing in seq 1
